






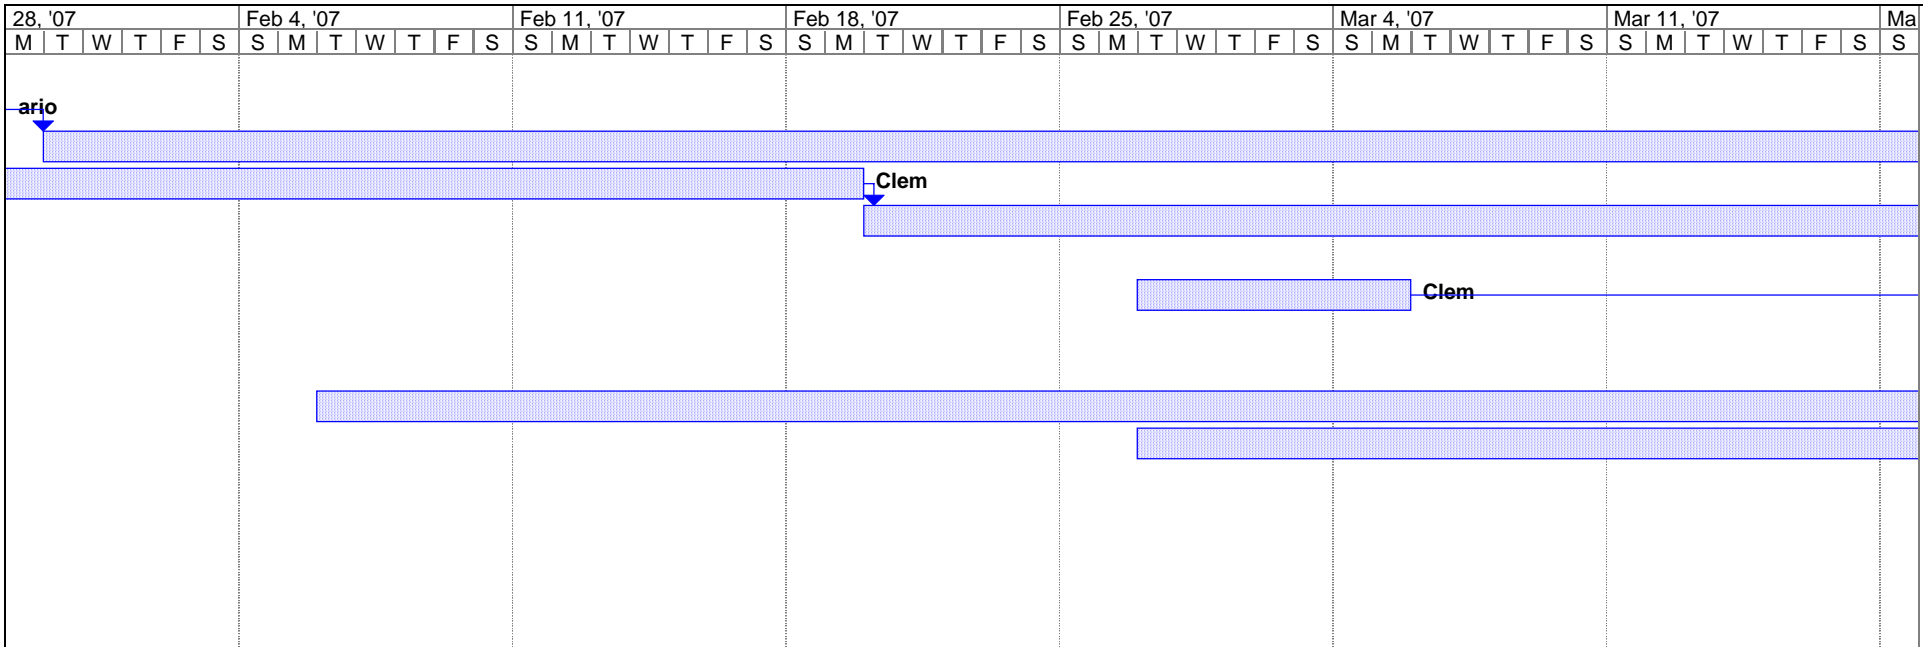


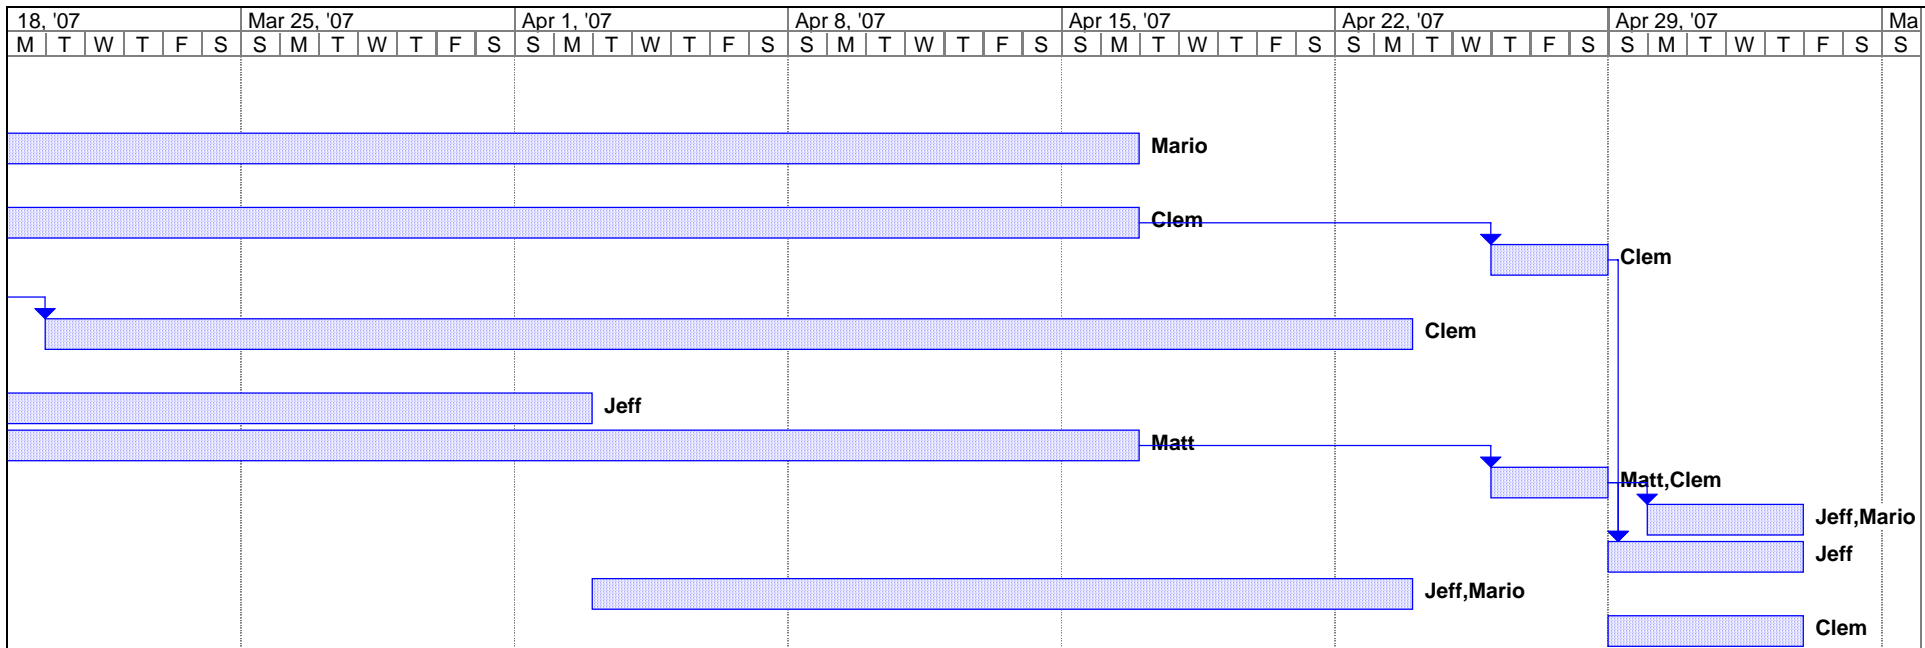


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	14, '07							Jan 21, '07							Ja				
							M	T	W	T	F	S	S	M	T	W	T	F	S	S					
1	Pick up microcontroller and Xbe	2 days	Tue 1/16/07	Wed 1/17/07		Mario																			
2	Determine which transceivers to	4 days	Tue 1/23/07	Fri 1/26/07		Matt,Mario																			
3	Integrate Sourceboost with the	77 days	Tue 1/30/07	Mon 4/16/07	2	Mario																			
4	Research the H-bridge	28 days	Tue 1/23/07	Mon 2/19/07		Clem																			
5	Design the H-bridge board	56 days	Tue 2/20/07	Mon 4/16/07	4	Clem																			
6	Build and test the H-bridge boai	3 days	Thu 4/26/07	Sat 4/28/07	5	Clem																			
7	Write PWM code for the H-bridg	7 days	Tue 2/27/07	Mon 3/5/07		Clem																			
8	Test code with H-bridges provid	35 days	Tue 3/20/07	Mon 4/23/07	7	Clem																			
9	Test new motors	1 day	Tue 1/23/07	Tue 1/23/07		Jeff																			
10	Create and test the hovercraft c	56 days	Tue 2/6/07	Mon 4/2/07		Jeff																			
11	Design the microcontroller boar	49 days	Tue 2/27/07	Mon 4/16/07		Matt																			
12	Build the microcontrollers	3 days	Thu 4/26/07	Sat 4/28/07	11	Matt,Clem																			
13	Test signal RSSI values with th	4 days	Mon 4/30/07	Thu 5/3/07	12	Jeff,Mario																			
14	Build two new hovercrafts	5 days	Sun 4/29/07	Thu 5/3/07	6,12	Jeff																			
15	Code the control algorithms in C	21 days	Tue 4/3/07	Mon 4/23/07		Jeff,Mario																			
16	Fine tune the motor speed cont	5 days	Sun 4/29/07	Thu 5/3/07		Clem																			

Project: Project1 Date: Thu 5/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Project1 Date: Thu 5/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Project1 Date: Thu 5/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
